



HALIBURTON, KAWARTHA, PINE RIDGE DISTRICT HEALTH UNIT

SEWAGE SYSTEM INSPECTION REPORT AND USE PERMIT

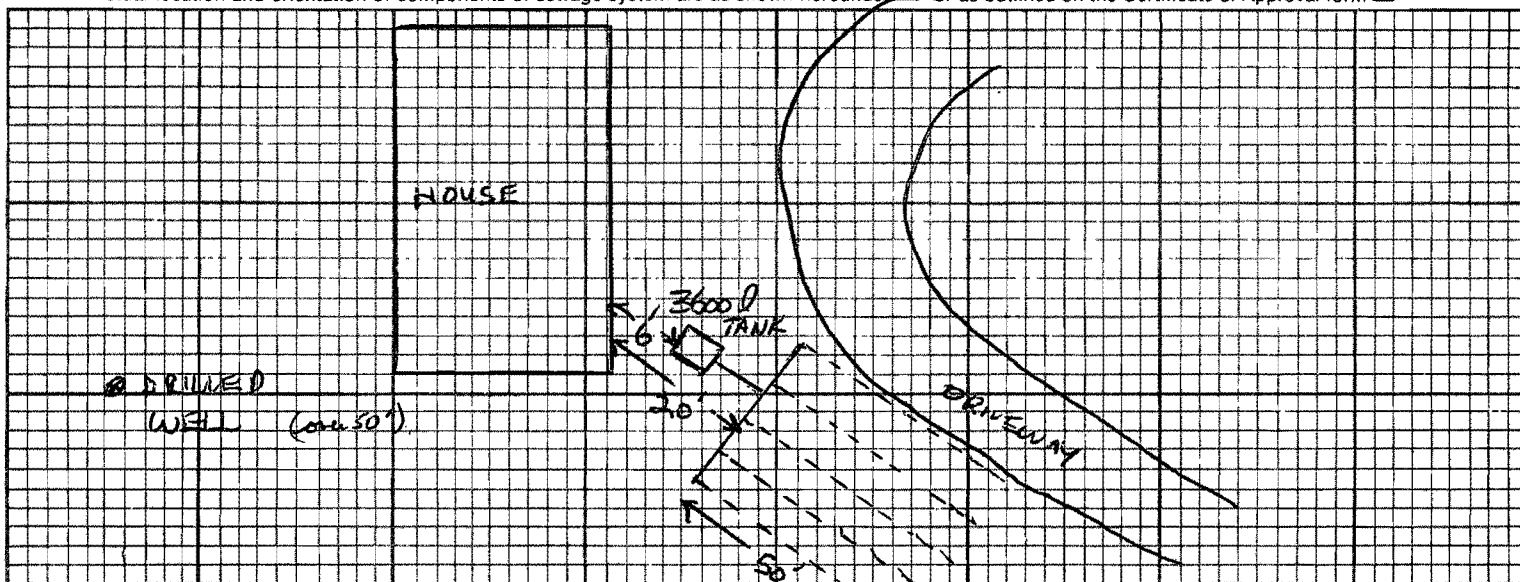
BX-19-92
FILE NUMBER

REPORT

DATE Oct 2/92INSTALLED BY: DAVE GRAHAM

Work authorized by certificate of approval has been satisfactorily completed and includes.

Septic Tank/Holding Tank of working capacity of 3600 litres constructed of steel/concrete/fiberglass on site ☐ or prefabricated ☒
to serve 3 bedrooms

Distribution Pipe: Type PVC ☒; Clay Tile ☐; Other ☐ Absorption Trench System ☒Filter Bed System ☐; Filter Bed Area sq. m.; Contact Area sq. m.Total 76 Lineal Metres in 5 runs of 15 metres and fed by gravity ☒; Siphon ☐; or Pump ☐Other Details Actual location and orientation of components of sewage system are as shown hereunder ☐ or as outlined on the Certificate of Approval form ☐

The following work remains to be completed: Backfill system and sod or seed ☐; Stabilize all sloped surfaces ☐; Finish grading to shed run-off and divert water around leaching bed ☐; Other connect system to dwelling, keep vehicular traffic off leached

USE PERMIT

Under section 78 of the Environmental Protection Act, 1990 and regulations and subject to the limitations thereof, a permit is hereby issued to

JOHN & ELIZABETH ROEfor the use and operation of the Class 4 Sewage System Installed/Altered under Certificate of Approval # BX-19-92such system being located on Lot INDIAN POINT Plan 259 Sub. lot 72 & 73Township/Municipality BEXLEY County VICTORIAInspected and Recommended by L. BlomDATE Oct 2/92 Issued [Signature] (Director)

NOTE: Section 76 of the Act provides that no change can be made to any building(s) or structures in connection with which this sewage system is used, if the operation or effectiveness of the sewage system will be affected by the change, unless a Certificate of Approval is obtained.
